





BAUCHI STATE OF NIGERIA

CONSTRUCTION AND UPGRADING OF SPORTING FACILITIES







INTRODUCTION:

This report is to present a full Executive **Summary** of all project works being executed in Tafawa Balewa Stadium Bauchi, Zaranda Hotel and Games village training pitch in Bauchi, for the Under 17th World Youth Championship which took place in Nigeria. The new looks carried by this facilities is indeed due to the huge amount of commitment, effort and great achievement made by **THE GOVERNMENT OF BAUCHI STATE, THROUGH THE ABLE LEADERSHIP OF HIS EXCELLENCY THE EXECUTIVE GOVERNOR OF BAUCHI STATE MALLAM ISA YUGUDA.**

PROJECT TEAM:

The Upgrading of the stadium is being carried out with well qualify professionals with determination to help achieved the goals and aspirations of Bauchi State government in the sporting world and it people. The project team was made up of the Sport Facility Consultants(Sports Solutions Limited), IDEAL Communication Limited as one of the contractor on site in charge of all IT project in the stadium and Zaranda Hotel respectively, supply and installations of the scoreboard, energy saving floodlights fittings, supply and installations of CCTV in the stadium, Provision of PAS, PABX, Two Communication Systems, general refurbishment of V-Sat at the TV Compound area repairs of the two number 500Kva existing generators in the stadium, While Zik's properties limited the second major contractor on site were commission to handle the construction and installations of two number artificial football pitches one in the main bowl of the stadium and the second pitch which is located at the games village for training both in Bauchi state capital, fencing of Games village training pitch, general painting of stadium, seats numbering and spraying, replacement of steel facial and aluminium facial at the VIP stand, repairs of ticket booth, repairs of gate, construction of additional public toilet at the main bowl of the stadium, expansion of the changing facility at the game village and also the extension and furnishing of the Sub Seat office in the Stadium. The team is also made up of Technical **Committee on Projects** in Bauchi State and the Ministry of youths and Sports as the Client ministry for the project.

PROJECT STATUS:

The quality of work done was quite satisfactory, with FIFA acknowledging Bauchi Sub-Seat as one of the best centre for the competitions. Below is a list of the project executed for the competitions by the government

PROGRESS & PERFORMANCES:

SERIAL Number	FACILITIES	REMARKS
1	Construction of a New VVIP Room as extension in the stadium.	Completed and Fully Furnish
2	Construction of a Press Conference Room as extension in the stadium.	Completed and Fully Furnish
3	Construction of a New Media Centre in the stadium	Completed with supply of fifty number Computers, Connected to Internet(LAN and WIRELESS) -3.16 GHz intel Core Studio 2,250GB HDD,2.0G RAM Window Vista,17" flat screen Full Multi Media. -Server (HP Rack, with Seven Switches, ML 360D XEON SERVER. Window server 2003. Provision of television set, printers, and photocopiers and other furniture as required by FIFA.
4	Medical Centre	Fully Upgraded and well Furnish with all the required medical equipment request by FIFA.
5	A New Scoreboard	Supply and installation completed and also construction of new stand to serve as scoreboard support in the stadium all complete. The scoreboard is the best in the country with the following Specifications: -P25mm Outdoor Full Color Led Display -Cabinet size:1000mm X 1000mm -Screen Size :12m(Wide)X 4 (Vertical) -Cabinet Number:12(Horizontal) X 4(vertical) -Screen Resolution:480pixels X 160pixels=76800pixels/Screen -Optimum Viewing Distance:20m,and can be seen from 200-300m away view site
6	A Closed Circuit Television(CCTV)	Supply and installations of the closed circuit systems in the stadium was successfully Completed. Twenty five Colour IR(Day and Night Vision) Cameras were install to help aid security, control and detect the acts of crime in the stadium enviroment, it also has

		a systems monitor and a thirty day capacity DVR recorder
7	Public Address System(PAS),PABX	Completed with about Forty number speakers at the popular side and four number at the grand stand and provision of PABX at all required positions at specified by FIFA.
8	Security Communication Equipment	Completed with twenty number two way communications radio sets with transceiver and base station, and ten number hand held metal detectors
9	Provision of a Battery Bank	Completed to serve as power backup
10	Floodlight	Upgrading of the stadium light from 900LUX to 1500LUX as required by FIFA.
11	Generator	Provision of a One number 1250Kva Generator in addition to the two number 500Kva in the Stadium. Repairs of existing 500Kva
12	Artificial Turf	Completed for both the Main Bowl and the Training Pitch in the games village
13	Fire Fighting Equipment	Completed and Provided at the required Position.
14	Camera Stands	All the four Number Required Position have been Upgraded and Completed.
15	Seat Numbering	All the Sectors in the Stadium have been Clearly marked and the Seats Number as required
16	Internet Facilities	C-BAND
17	Additional Public Toilet	Construction of Additional public toilet in the main bowl of ATBS Bauchi

FIFA MEDICAL REQUIREMENT:

In order to fulfil the stringent Medical requirements for the FIFA U-17 world cup. The following projects were undertaken:

- Construction of a new modern Accident And Emergency at the Specialist Hospital which has two fully equipped theatres, a mobile X Ray machine with auto processor, observation rooms, full facilities for basic and advanced life support, laboratory, pharmacy and offices.
- Upgrade of the ambulance at the Specialist Hospital Bauchi from Basic Life Support to Advanced Life Support facility at the Cost of Seven Million naira.



- Renovation of the Medical centre at the stadium and its furnishing and equipment to have a complete modern physiotherapy, radiological and medical equipment with advanced life support facility.
- Setting up of a standard ICU at the stadium with advanced life support in collaboration with FIFA and the Federal Government.

QUALITY OF WORKMANSHIP:




The level of workmanship that was put in place was quite impressive and of good quality. It also aid the Sub-Seat a price from FIFA as the best venue of the tournament.

STADIUM APPROACH VIEW



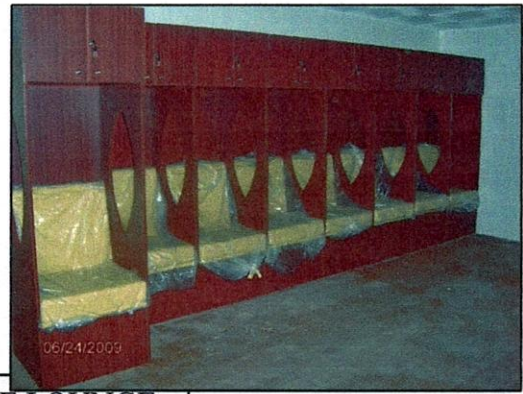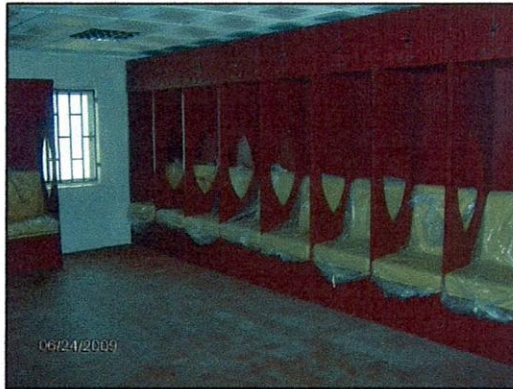

PRESS CONFERENCE LOUNGE

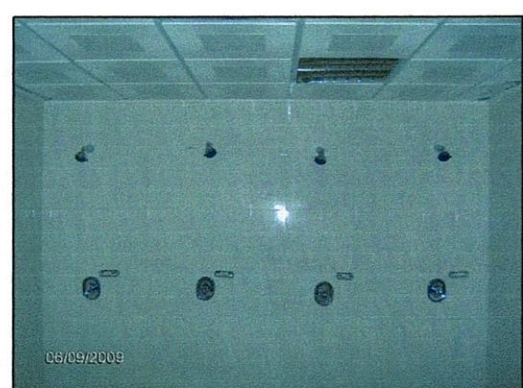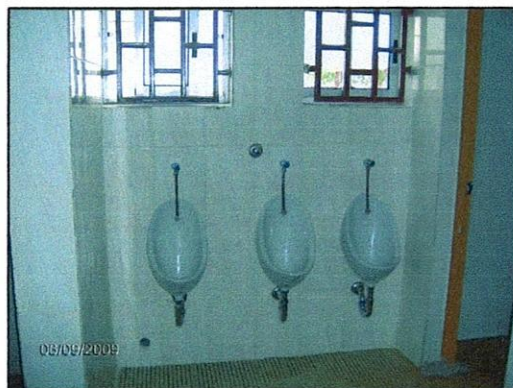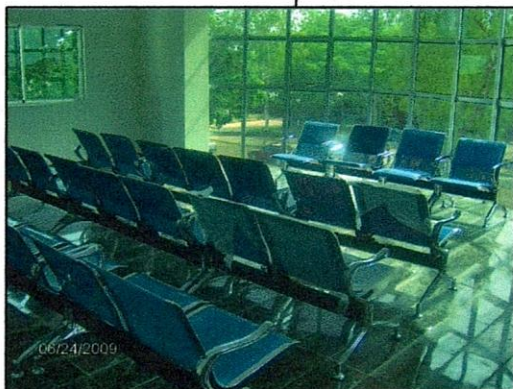

THE NEW VVIP LOUNGE




VIP LOUNGE




NEW VIP SEATS









MAIN BOWL ARTIFICIAL
PLAYING TURF

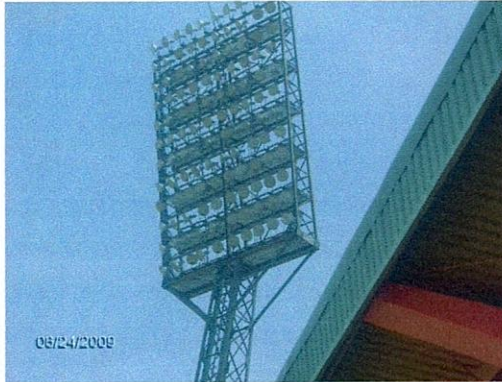



THE NEW MEDIA
CENTRE/FACILITIES





MEDICAL CENTRE FACILITIES

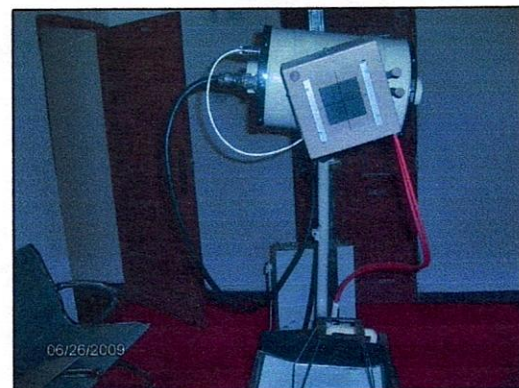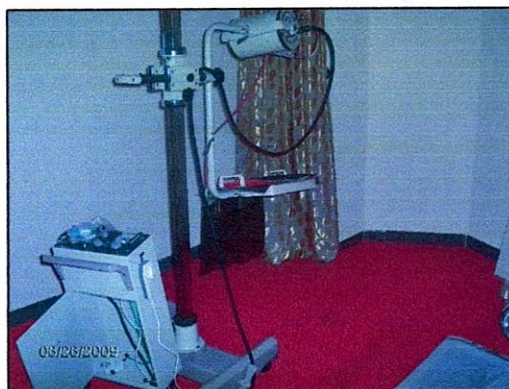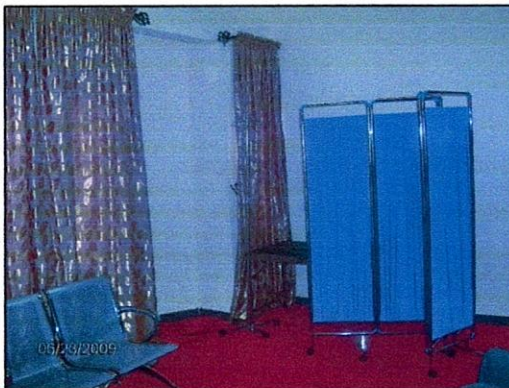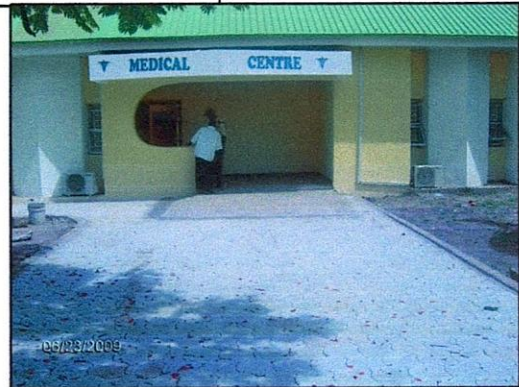


ZARANDA HOTEL BAUCHI

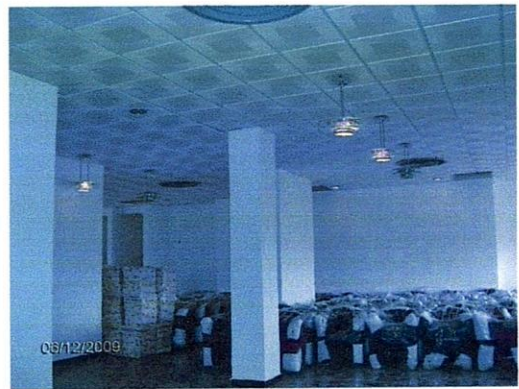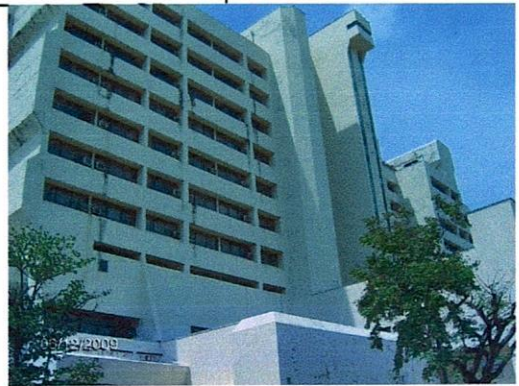

A & E UNIT SPECIALIST HOSPITAL BAUCHI STATE

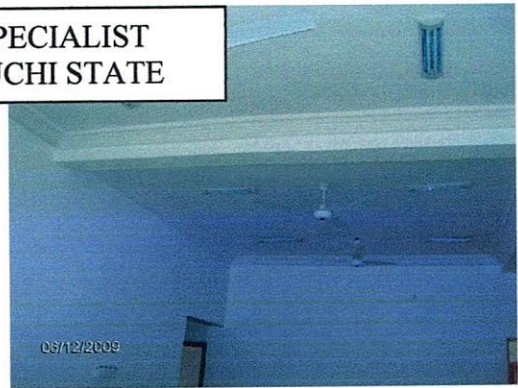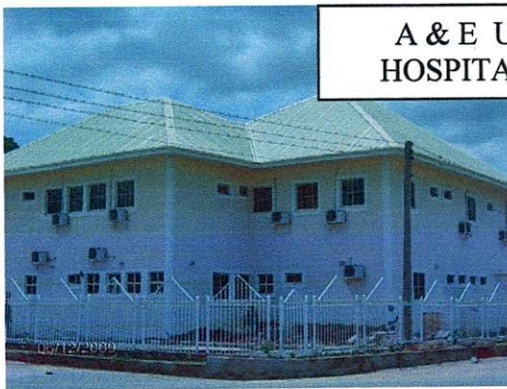

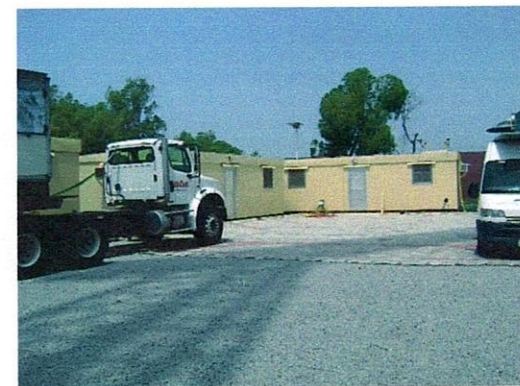

GENERAL REMARKS:

The Abubakar Tafawa Balewa Stadium is a **11,250 Capacity Stadium** with a Grand Stand which is made of the VIP sitting area of a total of about **Fifty Executive Leather Sitting** area, A press gallery comprising of the press working area, a three row of about thirty three seats as photographic area and an outside commentary position table as required by FIFA inspection team.

Three matches were played in Bauchi, with the following results:

DATE	COUNTRY A	SCORE	COUNTRY B	SCORE	REMARKS
30/10/2009	NIGERIA	2	ARGENTINA	1	Satisfactory
5/11/2009	KOREA	5	MEXICO	3	Satisfactory
8/11/2009	COLUMBIA	4	TURKEY	3	Satisfactory

MINISTRY OF YOUTH AND SPORTS, BAUCHI STATE

APPENDIX A

UPDATED OF ACHIEVEMENT MADE IN THE PROVISION OF FACILITIES BY THE GOVERNMENT OF BAUCHI STATE.

*Balewa project
already paid.*

S/ N	TITLE OF PROJECT	LOCATION OF PROJECT	DATE OF AWARD	CONTRACT SUM	AMOUNT PAID	LEVEL OF COMPLETION	REMARKS
1	Fencing of Games Village By EIA Nig Ltd	Games Village Bauchi	7/1/2009	N24,532,938.00	N13,266,469.00		
2	Supply and Installation of Artificial Turf at 2Nos.Football Field by Zik Properties Ltd	Abubakar Tafawa Balewa Stadium and the Games Village	20/10/2008	N166,441,066.10	N143,082,210.00	100%	<i>2 #23m?</i>
3	Renovation and Upgrading Of Medical Centre	ATBS,BAUCHI	20/4/2009	N17,116,450.00	N17,116,450.00	100%	Direct Labour by Project Office to meet FIFA standard For hosting of World U17 Soccer Tournament.
4	Renovation and Upgrading Of Main Gallery	Abubakar Tafawa Balewa Stadium, Bauchi	20/4/2009	N20,004,986.40	N20,004,986.40	100%	Direct Labour by Project Office to meet FIFA standard For hosting of World U17 Soccer Tournament.
5	Construction of VVIP Presidential Stand	Abubakar Tafawa Balewa Stadium, Bauchi	20/4/2009	N9,994,430.00	N9,994,430.00	100%	Direct Labour by Project Office to meet FIFA standard For hosting of World U17 Soccer Tournament.
6	Supply of Medical Equipment and Accessories	ATBS Bauchi Medical Centre	20/4/2009	N14,443,000.00	N14,443,000.00	100%	Direct Labour by Project Office to meet FIFA standard For hosting of World U17 Soccer Tournament
7	Seat and Seat Numbering	ATBS, Bauchi	20/4/2009	N5,000,000.00	N5,000,000.00	100%	"
8	Construction of Players Dressing Cabinet	ATBS, Bauchi	20/4/2009	N13,200,000.00	N13,200,000.00	100%	"
9	Supply and Installation of FIFA Standard LED						Direct Labour by Project Office to meet FIFA standard

	Display and Energy Saving Floodlight by Ideal Communication Ltd		7/5/2009	N198,000,000.00	N198,000,000.00	100%	For hosting of World U17 Soccer Tournament.
10	Construction of Media Centre	Abubakar Tafawa Balewa Stadium, Bauchi	20/4/2009	N8,648,209.00	N8,648,209.00	100%	Direct Labour by Project Office to meet FIFA standard For hosting of World U17 Soccer Tournament.
11	Supply of Computers to Media Centre at Abubakar Tafawa Balewa Stadium Complex, Bauchi by Tahir Agro Allied Co.	Abubakar Tafawa Balewa Stadium, Bauchi	9/9/09	N35,924,733.60	N35,924,733.00	100%	Direct Labour by Project Office to meet FIFA standard For hosting of World U17 Soccer Tournament.
12	Construction and installation of ultra-modern Water Treatment Plant at Abubakar Tafawa Balewa Stadium Complex, Bauchi	Abubakar Tafawa Balewa Stadium Complex Bauchi		N21,879,375.00	N21,879,375.00	100%	Direct Labour by Project Office to meet FIFA standard For hosting of World U17 Soccer Tournament.
13	Procurement and installation of CCTV and Public Address System for Security Surveillances at Abubakar Tafawa Balewa Stadium Complex, Bauchi	Abubakar Tafawa Balewa Stadium Complex Bauchi		N11,500,000.00	N11,500,000.00	100%	Direct Labour by Project Office to meet FIFA standard For hosting of World U17 Soccer Tournament.
14	Consultancy Services on Provision and upgrading of Sporting facilities in Bauchi Sub-Seat	Abubakar Tafawa Balewa Stadium Complex Bauchi	18/6/09	N15,925,326.79	N10,500,000.00	65.93%	
15	Supply of Computers and Internet Connectivity at ATBS and Media Centre by Tahir Agro Allied Ltd	ATBS and Media Centre, Bauchi	9/9/09	N35,924,733.60	N35,924,733.60	100%	

ADDITIONAL WORKS EXECUTED BY CONTRACTORS ON SITE.

APPENDIX B

S/ N	TITLE OF PROJECT	LOCATION OF PROJECT	DATE OF AWARD	CONTRACT SUM	AMOUNT PAID	LEVEL OF COMPLETION	REMARKS
1	Remodelling and Expansion Of Changing Facility for players as requested by FIFA	Games Village training pitch		N4,216,306.30	1	100%	Zik Properties Nigeria Limited
2	Construction of partition fence in Games village	Games Village training pitch		N3,416,170.00	1	100%	Zik Properties Nigeria Limited
3	Construction of Blockwall,Provision of Barricade,Steel fence work and grassing around the pitch	Games Village training pitch		N5,027,700.00	1	100%	Zik Properties Nigeria Limited
4	Construction of one number additional public toilet as requested by FIFA	ATBS ,BAUCHI		N5,912,445.00	1	100%	Zik Properties Nigeria Limited
5	Construction of Extension block for youth development programme and completion of LOC office	ATBS ,BAUCHI		N3,036,342.25	1	100%	Zik Properties Nigeria Limited
6	Provision of gate and Upgrading of TV Compound fence in the stadium	ATBS,BAUCHI		N1,617,000.00	2		Zik Properties Nigeria Limited

ADDITIONAL WORKS EXECUTED BY CONTRACTORS ON SITE							APPENDIX C
S/ N	TITLE OF PROJECT	LOCATION OF PROJECT	DATE OF AWARD	CONTRACT SUM	AMOUNT PAID	LEVEL OF COMPLETION	REMARKS
1	Ceiling works,Repairs of two Transformers,changing of Electrical lamps and fittings,Repolishing of wooden claddings,Fire Alarm System,Purchase and installation of 183 Elect Cards Locks,Servicing of two number 620KVA generator,Purchase of two number 200AH Battery and general maintenance	Zaranda Hotel		N22,278,532.80		100%	Ideal Communication Limited.
2	Construction of Six number players reverse beach.	ATBS,BAUCHI		N3,799.998.00		100%	Ideal Communication Limited.
3	Purchase and installation of one number Camera	ATBS,BAUCHI		N300,000.00		100%	Ideal Communication Limited.
4	Construction of Scoreboard base	ATBS ,BAUCHI		N2,200,000.00		100%	Ideal Communication Limited.
5	Construction of Scoreboard Housing	ATBS ,BAUCHI		N700,000.00		100%	Ideal Communication Limited.
6	Repairs of Parking light at the handball pitch.	ATBS,BAUCHI		N160,000.00		100%	Ideal Communication Limited.
7	Sycronisation of two number 500KVA generators	ATBS, BAUCHI		N2,300,000.00		100%	Ideal Communication Limited.
